

MEMORANDUM

DATE: May 31, 2017

TO: Brian Dissette
Bill Hunter

FROM: Daniel A. Dombos II, P.E.

RE: SRF #5602-01-2a Monroe Boulevard & Indian Grove Lift Station Project Update

Current Progress:


Kalin Construction is progressing in their work to complete the new Monroe Boulevard. Kalin's crews have been busy getting the lawn areas graded and topsoiled and raising manholes to final grade.

The new Indian Grove is ready and standing by for permanent utility services to bring it on line.

The City's electrical department is working with their contractor to remove the few remaining utility poles from the old electrical system.



Construction Schedule:

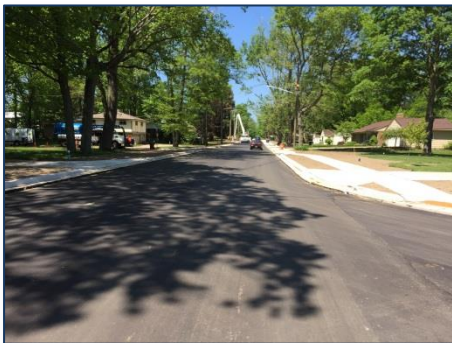

For the rest of this week, South Haven's electrical utility is scheduled to install the electrical service to the new Indian Grove Lift Station. Meanwhile, final connections will be made to put the new lift station on line.

Tree planting is scheduled to begin this week as well.

Following the lift station switch, Kalin will reroute the gravity sewer, demolish the old station, and remove the old pipes that cross back and forth over the creek. This work will require the crew to get back into Monroe

Boulevard near the creek. This was anticipated, and it will allow the completion of the remaining concrete work in that area.

Weekly "tailgate talks" continue to take place on Thursdays at 9:30 a.m. for anyone with project-related questions or needs. Those meetings are held at the intersection of Monroe Boulevard and Lovejoy Avenue.
