

## MEMORANDUM

DATE: April 26, 2017


TO: Brian Dissette

FROM: Jason W. Marquardt, P.E.

RE: North Beach Park Improvement and Paving Project

### **North Beach Park Improvement Project**

Milbocker & Sons continues to work on concrete sidewalk installation throughout the project limits. Rough grading and aggregate base for the roadway is currently being installed between concrete pours. Over the next few weeks, final grading along the roadway will be completed, and grading of the triangular parking area will commence. Asphalt paving is scheduled at the end of the project once all concrete work and grading is completed for the entire site. Site amenities will be installed as they become available.

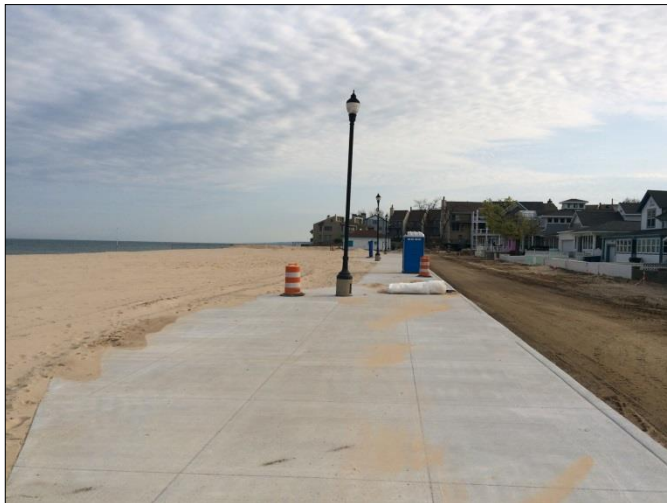

### **North Beach Paving Project**

Compton, Inc. continues to work on water services and minor water main work. Expect all water main and service work to be completed by the end of this week. Removals will start on concrete sidewalk areas scheduled for replacement. This work is expected to be completed by May 12 prior to milling of the existing streets and final asphalt paving.

Tailgate talks for both projects will be completed every week on Tuesday at 3:00 pm at the Monroe Park Area. For anyone who has specific questions or comments, please feel free to contact me at (269) 926-4565.
